### **TUKWILA PUBLIC SAFETY PLAN**

Monthly Update September 30, 2017

### Overall Plan

### Outreach

 Siting Advisory Committee presented to Council on the success of the August open house.

### Financial Oversight Committee

• First meeting was held June 29; scheduled to meet again in October.

### Siting Advisory Committee

 Siting Advisory Committee met again September 27. The agenda included an update on facility/property analysis, discussion of winter Open House, bylaws review and October meeting date.

### Near-term Council Decisions and Key Dates

 October 2 and 16, Council Executive Session Site Selection Update (Executive Session due to the potential to affect value of property)

### Fire Stations

### Siting

- Heartland with SOJ and City of Tukwila has continued to review the list of potential sites and have narrowed these down to a short list based upon the approved siting criteria.
   Short list was shared with Council at the September 5 Executive Session.
- Architect is investigating feasibility of the potential sites from a design perspective while Heartland and SOJ are continuing to further investigate the potential sites and refine the list based upon the approved siting criteria.
- The next Executive Session with Council will be held October 2, and potentially the 16<sup>th</sup> as well, which will include additional information from initial environmental studies, architect feasibility studies and estimates.

### Architecture and Programming

- Architectural program has been reviewed and approved by the team.
- Schematic Design for 51 has begun.
- Project team will present design update to all fire staff on October 5.

### Design and Permitting

Schematic Design phase began for Station 51 in late August.

• Phases scheduled to begin for 52 and 54 in June, 2018.

### Bidding and Construction

- Phases scheduled to begin for 51 in September, 2018.
- Phases scheduled to begin for 52 and 54 in July, 2019.
- The competitive bid process for a GC/CM contractor is underway with staff selection in October and Council Approval in November. Preconstruction services to begin late November.

### **Justice Center**

### Siting

- Heartland with SOJ and City of Tukwila has continued to review the list of potential sites
  and have narrowed these down to a short list based upon the approved siting criteria.
   Short list to be shared with Council at the September 5 Executive Session.
- Architect is investigating feasibility of the potential sites from a design perspective while
  Heartland and SOJ are continuing to further investigate the potential sites and refine the
  list based upon the approved siting criteria.
- The next Executive Session with Council will be held October 2, and potentially the 16<sup>th</sup> as well, which will include additional information from initial environmental studies, architect feasibility studies and estimates.

### Architecture and Programming

 DLR has begun programming efforts and has held several meetings with courts, emergency management and police staff to talk through the needs and scope.

### Design and Permitting

• Phases scheduled to begin in November, 2017.

### **Bidding and Construction**

• Phases scheduled to begin in December, 2018.

### **Public Works Facility**

### Siting

- Heartland with SOJ and City of Tukwila has continued to review the list of potential sites
  and have narrowed these down to a short list based upon the approved siting criteria.
   Short list to be shared with Council at the September 5 Executive Session.
- Architect is investigating feasibility of the potential sites from a design perspective while
  Heartland and SOJ are continuing to further investigate the potential sites and refine the
  list based upon the approved siting criteria.

The next Executive Session with Council will be held October 2, and potentially the 16<sup>th</sup>
as well, which will include additional information from initial environmental studies,
architect feasibility studies and estimates.

### Architecture and Programming

• Phases scheduled to begin in 2018.

### Design and Permitting

Phases scheduled to begin in June, 2018.

### Bidding and Construction

• Phases scheduled to begin in September, 2019.

### Budget

Attached.

### Schedule

### October

- Fire Station GC/CM Proposals Received
- Council Executive Session(s) on Siting
- Public Safety Plan Sting Advisory Committee Meeting
- Financial Oversight Committee Meeting
- DBE recommendation to Public Safety Committee
- Financing the budget gap philosophy development in Finance Committee

### November

- Fire Station GC/CM Interviews and Selection
- Fire Station GC/CM Pre-Construction Contract to Public Safety Committee and Council
- Fire Stations 52 and 54 final sites selection
- Justice Center final site selection
- Justice Center CPARB Application Submitted for GC/CM approval

### December

- Open House #3
- Public Safety Plan Siting Advisory Committee Report
- Fire Stations final program review and pricing to Public Safety Committee and Council

- Justice Center GC/CM Contractor Solicitation
- Justice Center programming update

### January 2018

 Justice Center contractor pre-construction contract to Public Safety Committee and Council

### February 2018

• City shops architect contract to Public Safety Committee and Council

### March 2018

• City Shops facility site selection

### **April 2018**

• City Shops facility programming update

### May 2018

• Fire Station 51 Construction Contract Approval to Public Safety Committee and Council

### June 2018

- Fire Station 52 and 54 schematic design begins
- City Shops facility program update

### July 2018


• Final contracting method determination for City Shops facility

### August 2018

• Fire Station 51 subcontractor bid procurement begins

TUKWILA PUBLIC SAFETY PLAN FACILITIES PLAN

Project Schedule

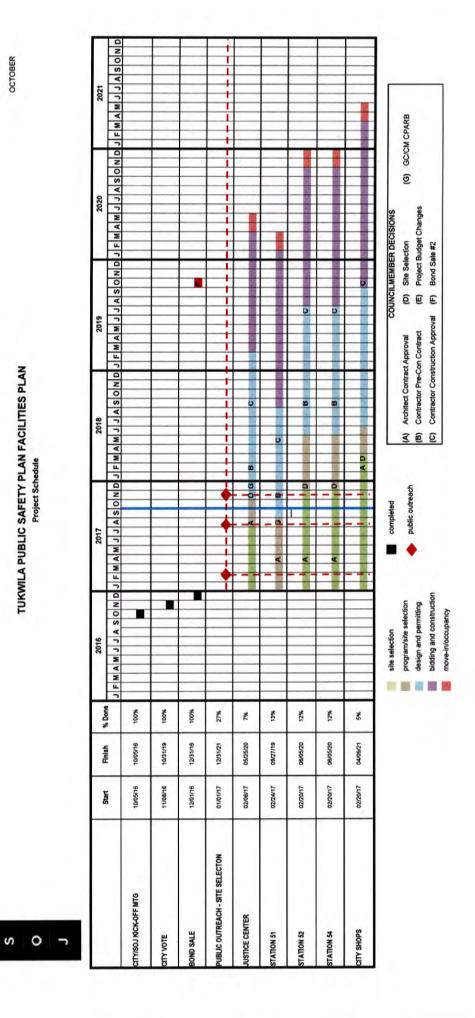



# City of Tukwila - Public Safety Plan Conceptual Budget Summary YOE \$ (in thousands)

### PUBLIC SAFETY PLAN - FUNDING

	ΥE	YEAR OF EXPENDITU	IDITURE (YOE) SUMMARY	MAKY		
Project	1	JTGO	Impact Fees	<b>General Fund</b>	<b>Enterprise Funds</b>	Total
<u>Facilities</u>						
Public Safety Building	↔	28,629 \$	•	•	<del>\$</del> - <del>\$</del> -	38,629
Fire Stations (51, 52, 54)		18,824	4,750	858	ı	24,432
Public Works Shops		ı	•	14,747	14,746	29,493
FACILITIES TOTAL	s	47,453 \$	4,750	\$ 15,605	\$ 14,746	82,554

29,932 **112,486** 14,746 15,605 \$ 4,750 29,932 **\$ 77,385 \$** PLAN TOTAL Apparatus/Equipment

indicates voter approved

as of December 31, 2016

## PUBLIC SAFETY PLAN - FACILITIES

				rile Station Program			
Project Budgets (in YOE \$)	Public Bui	Public Safety Building	FS 51	FS 52	FS 54	City Shops	TOTAL
Category							
A/E Services (both design & CA)	&	1,616	\$ 731	\$ 356	\$ 464	\$ 698	\$ 4,037
Land Acquisition		6,000	0	653	862	000'9	13,516
Permits/Fees		440	255	88	116	522	1,421
Construction (pre-con, const & tax)		16,195	7,809	3,278	4,273	19,202	50,758
Construction Related Costs		1,064	1,047	438	551	425	3,526
PM Services (incl Other Professional Svcs)		1,114	460	297	397	348	2,615
Contingency (incl Construction & Project)		2,199	1,145	546	999	2,127	6,682
TOTAL	ઝ	28,629 \$	\$ 11,446 \$	\$ 5,657	\$ 7,329	\$ 29,493	\$ 82,554



### CITY OF TUKWILA Public Safety Plan Fire Stations - 51, 52, 54 Conceptual Budget Summary YOE \$ (in thousands)

### FUNDING SOURCE - Based on Initial Project Costs

YEAR OF EXPENDITURE (YOE) SUMMARY								
Project	UTGO (voter	Impact Fees	General Fund	Enterprise Funds	TOTAL			
Fire Stations	18,824	4,750	858	- (-)	24,432			
Justice Center	28,629	(4)		- TA-	28,629			
Public Works Shop			14,747	14,746	29,493			
Facilities Total	47,453	4,750	15,605	14,746	82,554			
Fire Apparatus/Equipment	29,932				29,932			
Public Safety Plan Total	\$ 77,385	\$ 4,750	\$ 15,605	\$ 14,746	\$ 112,486			

### **PROJECT COSTS**

Fire Station Program - INITIAL BUDGET ESTIMATE							
Project Category	FS51 17,950 sf	FS 52 6,567 sf	FS 54 8,228 sf	<b>TOTAL</b> 32,745 sf			
A/E Services (both design & CA)	731	356	464	1,551			
Land Acquisition		653	862	1,515			
Permits/Fees	255	89	116	460			
Construction (pre-con, const, tax)	7,809	3,278	4,273	15,360			
Construction Related Costs (incl bond)	1,047	438	551	2,036			
PM Services (incl other prof svcs)	460	297	397	1,154			
Contingency (incl Construction & Proj)	1,145	546	665	2,356			
TOTAL	\$ 11,446	\$ 5,657	\$ 7,329	\$ 24,432			

Fire Station Program - REVISED BUDGET ESTIMATE (as of 5/23/17)						
Project Category	FS51 <sup>1</sup> 9,426 sf	FS 52 <sup>1</sup> 15,068 sf	FS 54 9,287 sf	<b>TOTAL</b> 33,781 sf	FUNDING GAP	
A/E Services (both design & CA)	635	1,052	626	2,314	763	
Land Acquisition	653	-	862	1,516	1	
Permits/Fees	166	301	164	631	172	
Construction (pre-con, const, tax)	6,324	9,547	6,233	22,105	6,744	
Construction Related Costs (incl bond)	657	1,184	709	2,550	514	
PM Services (incl other prof svcs)	300	576	305	1,181	28	
Contingency (incl Construction & Proj)	749	1,094	765	2,608	252	
TOTAL	\$ 9,486	\$ 13,755	\$ 9,665	\$ 32,906	\$ 8,474	

<sup>1</sup> The main fire station was originally identified as FS51, but has been changed to FS52 in the revised	d estimate.
	,
